cloudspaces

CloudSpaces: Open Service Platform for the Next Generation of Personal Clouds

Ivan Utgé Hernández

Universitat Rovira i Virgili

SEVENTH FRAMEWORK PROGRAMME

UNIVERSITAT ROVIRA I VIRGILI

CloudSpaces Management













CloudSpaces Management

95% communication online
5% communication offline (meetings)

ONLINE connections: straight to the point and clear words
OFFLINE connections improve further ONLINE connections











CloudSpaces Management

Consortium meeting

Host: URV

Place: Barcelona

Date: April 2013

1. Recap of DoW tasks
2. Plan for the next months
3. Technicians coming from each partner, working together in the same room
4. Open dialogue (comments, improvements, questions,...)
5. Meeting each other, personally (face to face)

CloudSpaces Management

Management issues overcome

1. Modification of Canonical legal identity in Consortium
2. New technicians coming in the project (Industrial Partners)
3. Some internal deadlines were not accomplished → Tasks were rescheduled
4. Only two tasks were rescheduled for the second year:
   - *A3 (Generation of traces from U1 and eyeOS)*
   - *A14 (eyeCalendar integration with U1DB)*

CloudSpaces Management

Estimated person months (first year)

Partner	WP1	WP2	WP3	WP4	WP5	WP6	TOTAL
URV	12	24	22	30	20	6	114
EPFL		16		37	2	7	62
EUR		6	55	5		5	71
CNC		6	15	12	15	7	55
EOS		20			44	8	72
TST		24	15	12	15	6	72
1st Year	**12**	**18**	**20**	**16**	**12**	**18**	**96**

Real person months (first year)

Partner	WP1	WP2	WP3	WP4	WP5	WP6	TOTAL
URV	3,6	15,23	14,64	6,76	9,52	1,02	50,77
EPFL		9		13		2	24
EUR		2	18,48	1,01		1,26	22,75
CNC		0,74			4,39	0,37	5,5
EOS		7,41			14,85	0,32	22,58
TST		8,05	10,08	4,03		2,01	24,17
1st Year	**3,6**	**42,43**	**43,2**	**24,8**	**28,76**	**6,98**	**149,77**

CloudSpaces Management

Reasons for the deviation on the Person Months use:

- PMs should be adapted to the real needs of the project (we needed more human resources than expected)
- Some partners used fellows to work on the project. A fellow is someone who is learning by doing, with no previous experience, so his performance is lower than an engineer.

CloudSpaces Management

Financial management - Use of Resources

Partner	Costs	Average Budget	Prefinancing
URV	208.091 €	214.767 €	343.627 €
EPFL	170.299 €	158.609 €	253.774 €
EUR	174.956 €	157.003 €	251.204 €
CNC	57.626 €	150.000 €	240.000 €
EOS	103.398 €	125.594 €	200.950 €
TST	105.390 €	73.695 €	117.911 €
TOTAL	**819.760 €**	**879.666 €**	**1.407.466 €**

Total costs of the project in the first year were less than expected

Prefinancing covers the sum of those who spent more than expected

CloudSpaces Management


www.cloudspaces.eu

The project website has been updated periodically, including new documentation as deliverables or other useful publications.


We also published a news section to spread the word of dissemination actions done by all partners.

The twitter widget in the web, shows all the cloudspaces twits about the project and personal cloud news (@cloudspaces)

CloudSpaces Management

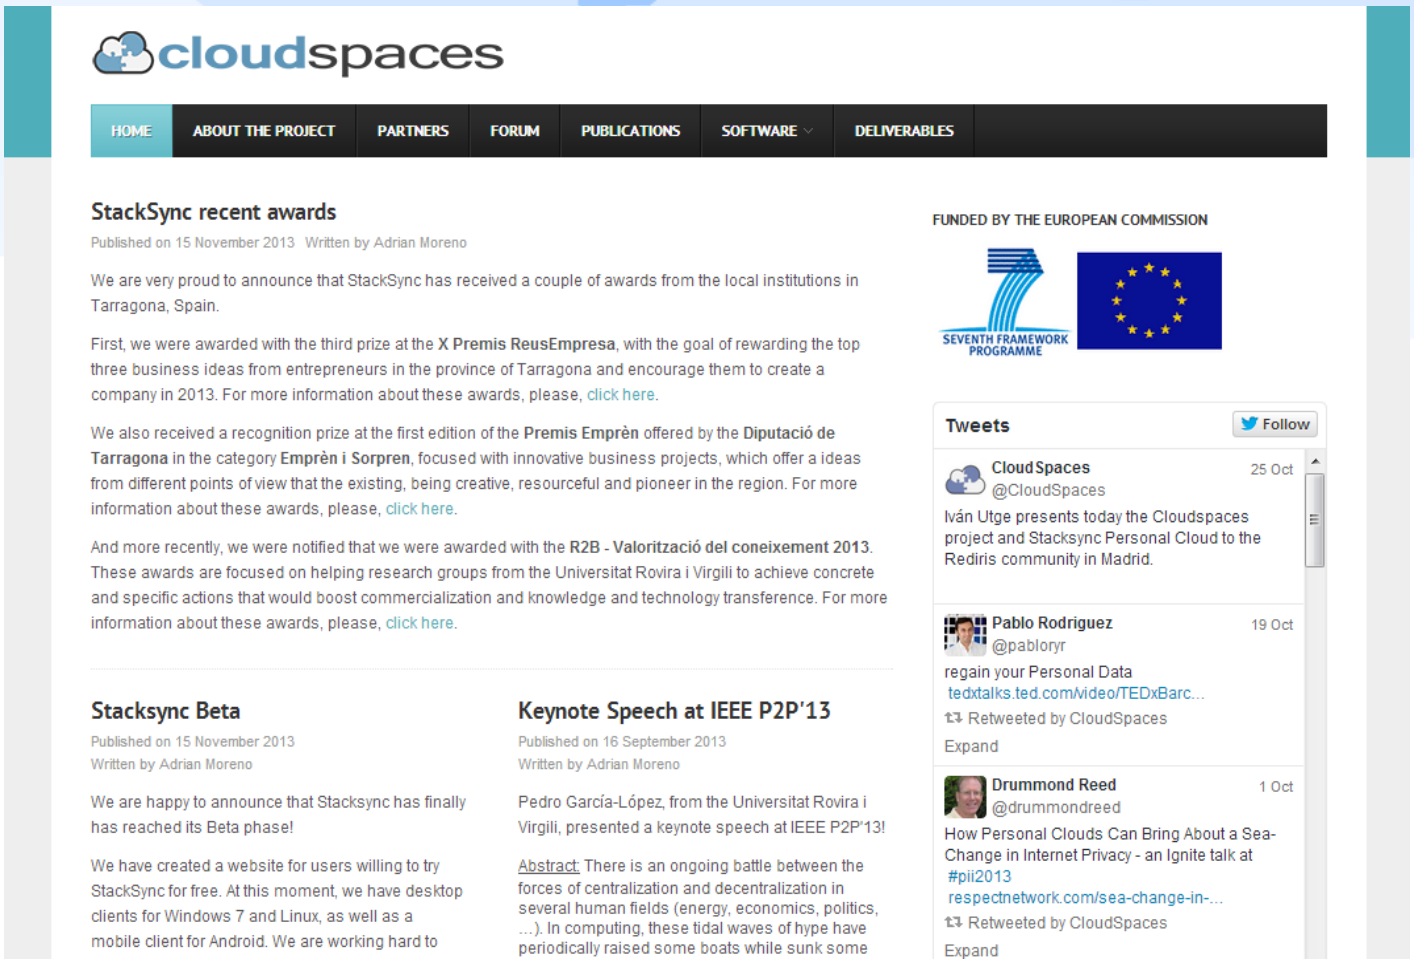

CloudSpaces Management

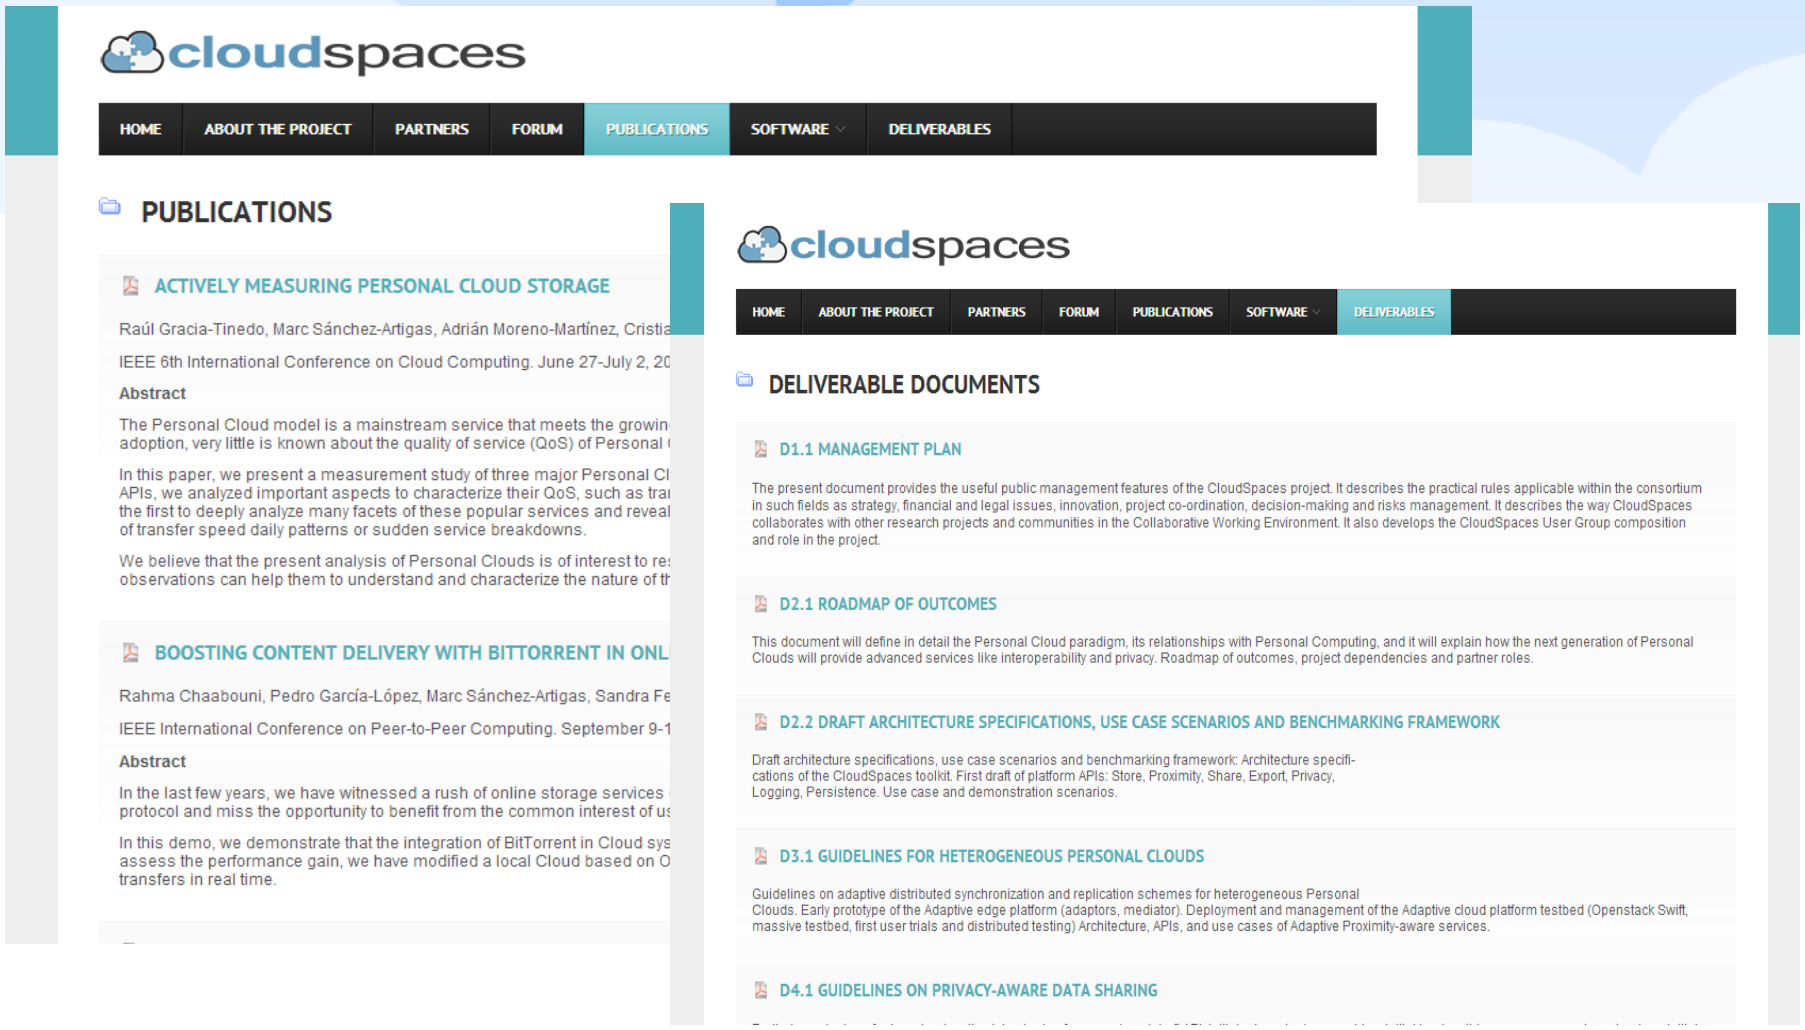

CONTACT DETAILS

Ivan Utgé Hernández

Universitat Rovira i Virgili
Departament d'Enginyeria Informàtica I Matemàtiques
Av.Paisos Catalans 26, Campus Sescelades
43007 Tarragona, Spain

ivan.utge@urv.cat
www.cloudspaces.eu
